



**Future Oxfordshire Partnership
Public Meeting – 3rd October 2024**
Oxfordshire County Council
Growth Deal infrastructure schemes

WANTAGE EASTERN LINK ROAD



A new road between the A417 and the A338. OCC is delivering the middle section of the scheme with St Modwen delivering the sections on either end.



Galliford Try commenced main civils works in **Oct 2023**.

WANTAGE EASTERN LINK ROAD



BENSON RELIEF ROAD



West section of a new road from the A4074 to the B4009. This will provide new developments to the north of Benson with direct access to the highway network.

In construction since **Jan 2024** and on target to complete in **Autumn 2024**




NORTH OXFORD CORRIDOR KIDLINGTON ROUNDABOUT

A44 corridor improvements at the Kidlington Roundabout. Will increase public transport capacity and reduce bus journey times as well as improved cycling and pedestrian facilities.

M40 J10 PADBURY ROUNDABOUT



Installation of site cabins during site setup phase

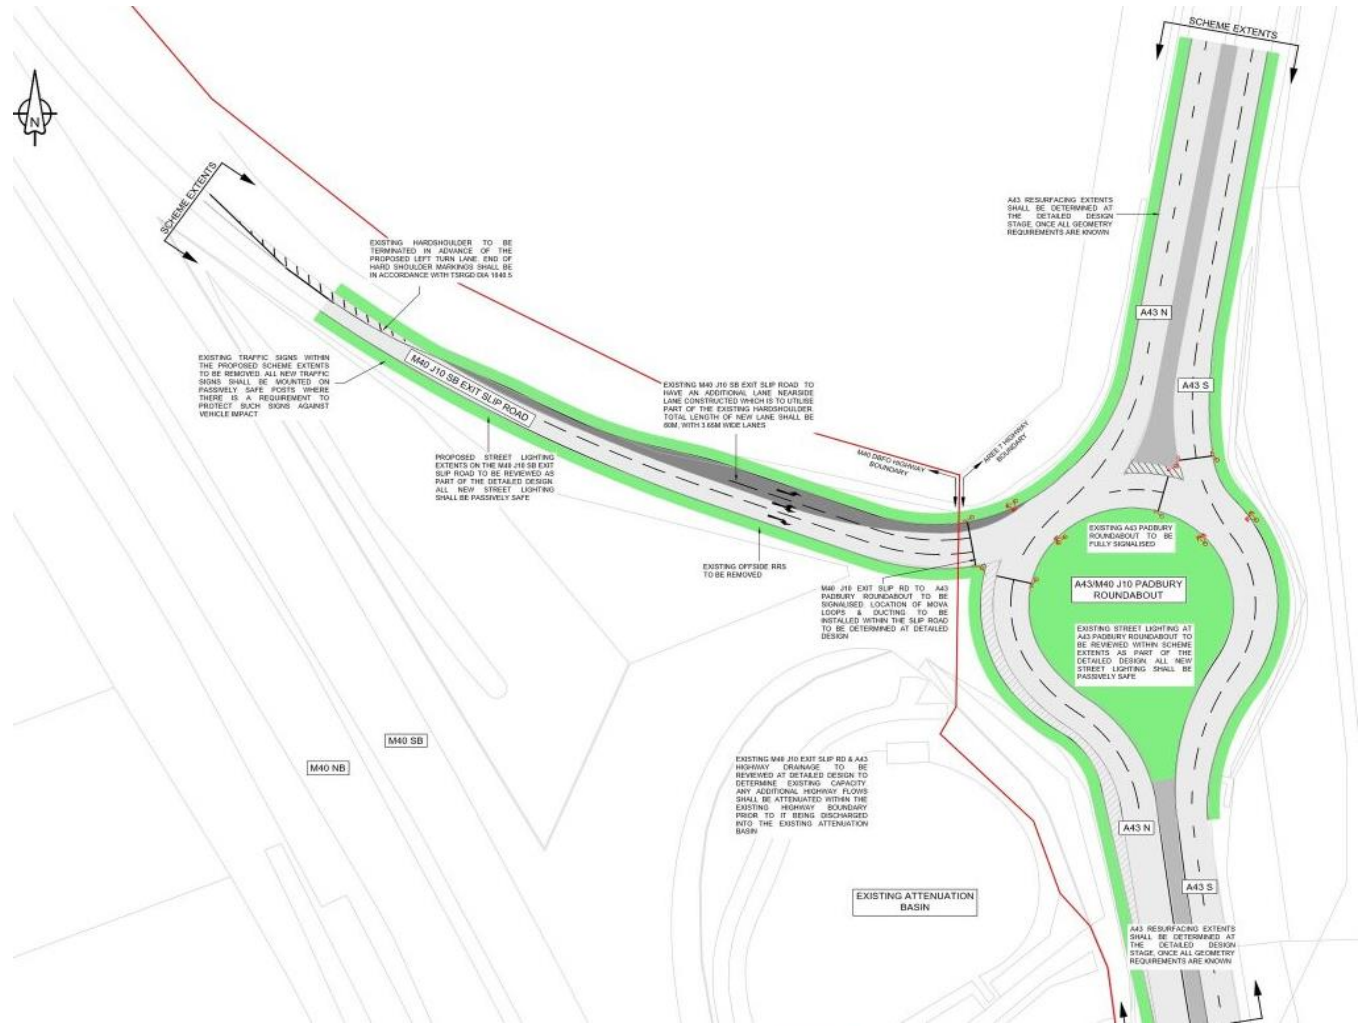

Removal of topsoil and site clearance



WOODSTOCK ROAD CORRIDOR

Construction:

- **St Margaret's West – North Side** - Kerbs laid from the top corner to the tree. Kerbs also laid for the landscape section. Tactile paving now laid.
- **Bevington Road – North Side** – Kerbs laid from north side across to the front of existing island. Removed remainder of kerbs and excavated footpath section on the northern side.
- **Field House Drive – North Side** – Finished. South Side – Broken out kerbs and tarmac around the junction, laying kerbs 03/09/24. Excavated footway within Field House Drive.
- **Bus Lane Reversal** - Hydroblasting works started on 02/09 and progressed well, completed most of the work within 5 days ahead of programme. Potential to be complete earlier than expected, however with lead in times, ETRO will still need to go live on 23 September.



BANBURY ROAD ROUNDABOUT



This scheme will improve the junction at the A4095/B4100 Banbury Road Roundabout in Bicester to support housing and employment developments in the Bicester Eco Town.

In construction since March **2024**; and on target to be completed by **Feb 2025**

BANBURY ROAD ROUNDABOUT



Installation of ducting, kerbing, and drainage along A4095 Southwold Lane
